



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

NAME: PRATHAM KUMAR

SRN NO.: PES2UG24CS368

PRN NO.: PES2202400086

ASSIGNMENT WORK

Objective:

Use Jira to turn functional requirements into Agile backlog items, simulate a sprint, and analyse progress.

Learning Outcomes:

By the end of this lab, students will be able to:

- Define and create Epics and User Stories in Jira using Agile conventions, ensuring clarity in functional requirements and end-user goals.
- Prioritize backlog items based on business value and user needs, and organize them in a structured Agile backlog.
- Assign Story Points to User Stories using the Fibonacci sequence to estimate effort, complexity, and uncertainty.
- Apply Planning Poker as a collaborative estimation technique to foster team alignment on task difficulty.
- Simulate a Sprint by creating Sprint 1 in Jira, populating it with selected backlog items, and progressing tasks across To Do In Progress Done. → →
- Monitor Sprint progress using Jira's Burndown Chart to track work completion against planned velocity.
- Reflect on team performance and Agile workflow through group discussion and analysis of Sprint outcomes.

Deliverables:

- Screenshot of:
 - Jira backlog with Epics and User Stories.
 - Story point assignments.
 - Sprint board (Active Sprint view).
 - Burndown Chart.
- A brief document answering the reflection questions.



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Step 1: Creation of Scrum Project in Jira

A new **Company-managed Scrum** project named “**Podcast Guest Scheduling & Outline Builder Project**” was created in Jira based on the requirements identified in Lab 1. The Scrum framework was selected to organize the project backlog, manage user stories, plan sprints, and track the progress of development activities.

The screenshot displays the Jira web interface for a Scrum project. The browser tabs at the top include 'Capstone Project - Process Tim...', 'SOFTWARE_ENGINEERING - Un...', 'Lab_2_Jira_Student_Handout.p...', and 'PGSOBP board - Scrum Board'. The address bar shows the URL 'prathamkumar041104.atlassian.net/jira/software/c/projects/PGSOBP/boards/3'. The Jira sidebar on the left lists navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Recent', 'Podcast Guest Scheduling...', 'PGSOBP board', 'Podcast Guest Scheduling & Outlin...', 'More spaces', 'Filters', 'Dashboards', 'Loom', 'Teams', 'Goals', 'Projects', and 'Customize sidebar'. The main content area shows the 'Podcast Guest Scheduling & Outline Builder Project' with the 'PGSOBP board' selected. The board is in 'Active sprints' view, showing three columns: 'TO DO', 'IN PROGRESS', and 'DONE'. The 'TO DO' column contains a large blue circular arrow icon and the text 'Get started in the backlog' and 'Plan and start a sprint to see work here.' with a 'Go to Backlog' button. The 'IN PROGRESS' and 'DONE' columns are currently empty.



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Step 2: Creation of Epics

The functional requirements identified in Lab 1 were grouped into major functional themes and created as **Epics in Jira**. Four Epics were created: **Interview Scheduling & Availability Management, Guest Information & Content Collection, Calendar & Notification Integration, and Episode Outline & Production Preparation**. These Epics represent the major areas of functionality in the Podcast Guest Scheduling & Outline Builder and will be further divided into related User Stories for backlog planning.

The screenshot displays the Jira web interface for the 'Podcast Guest Scheduling & Outline Builder Project'. The 'PGSOBP board' is selected, showing a list view of four epics. The interface includes a sidebar with navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', and 'Filters'. The main content area shows the epics with their respective assignees, reporters, priorities, and statuses.

Work	Assignee	Reporter	Priority	Status
PGSOBP-1 Interview Scheduling & Availability Manag...	Unassigned	Pratham Kumar	High	To Do
PGSOBP-2 Guest Information & Content Collection	Unassigned	Pratham Kumar	High	To Do
PGSOBP-3 Calendar & Notification Integration	Unassigned	Pratham Kumar	Medium	To Do
PGSOBP-4 Episode Outline & Production Preparation	Unassigned	Pratham Kumar	High	To Do



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Step 3: Creation of User Stories and Story Point Estimation

The Epics were further divided into **nine User Stories** based on the functional requirements and the roles of the Podcast Guest and Show Host. Each User Story was written using the Agile format “**As a [user role], I want [goal], so that [benefit]**” and linked to its corresponding Epic. Priorities were assigned according to user impact, and Story Points were estimated using the **Fibonacci scale** based on the relative effort, complexity, and uncertainty of each story. The complete backlog has an estimated effort of **33 Story Points**.

The screenshot displays the Jira Backlog for the 'PGSOBP board'. The interface includes a search bar, navigation tabs (Summary, Timeline, Backlog, Active sprints, Calendar, Reports, List, Forms, Goals, Components, Development, Code, Releases), and a 'Create sprint' button. The backlog contains 9 items, each representing a user story. Each story is a checkbox item with a description, a status dropdown, and a story point value. The total story points for the backlog are 33.

Item	Description	Status	Story Points
PGSOBP-5	As a Podcast Guest, I want to view available interview slots, so that I can choose a suitable date and time for my podc...	Interview Scheduling	3
PGSOBP-8	As a Podcast Guest, I want to submit my biography links and discussion topics, so that the Show Host can prepare rel...	Guest Information	3
PGSOBP-13	As a Show Host, I want to generate a formatted PDF production sheet from the episode outline, so that I can use it d...	Episode Outline & ...	3
PGSOBP-12	As a Show Host, I want to generate a structured run-of-show episode outline using the guest information and discus...	Episode Outline & ...	5
PGSOBP-11	As a Show Host, I want to receive a calendar invitation when a guest books an interview slot, so that I can keep trac...	Calendar & Notific...	3
PGSOBP-10	As a Podcast Guest, I want to receive a calendar invitation after booking an interview slot, so that I can keep track of...	Calendar & Notific...	3
PGSOBP-9	As a Show Host, I want to review the guest's submitted biography and discussion topics, so that I can prepare effecti...	Guest Information	3
PGSOBP-7	As a Show Host, I want to create and manage interview availability slots, so that Podcast Guests can book interviews ...	Interview Scheduling	5
PGSOBP-6	As a Podcast Guest, I want to book an available interview slot, so that I can confirm my podcast interview at a conven...	Interview Scheduling	5



Department of CSE, PES University


UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Product Backlog Prioritization: The product backlog was organized by prioritizing the user stories according to their functional importance and logical dependencies. Each user story was associated with the appropriate Epic, assigned a priority, and estimated using story points. The finalized backlog consists of 9 user stories with a total estimate of 33 story points.

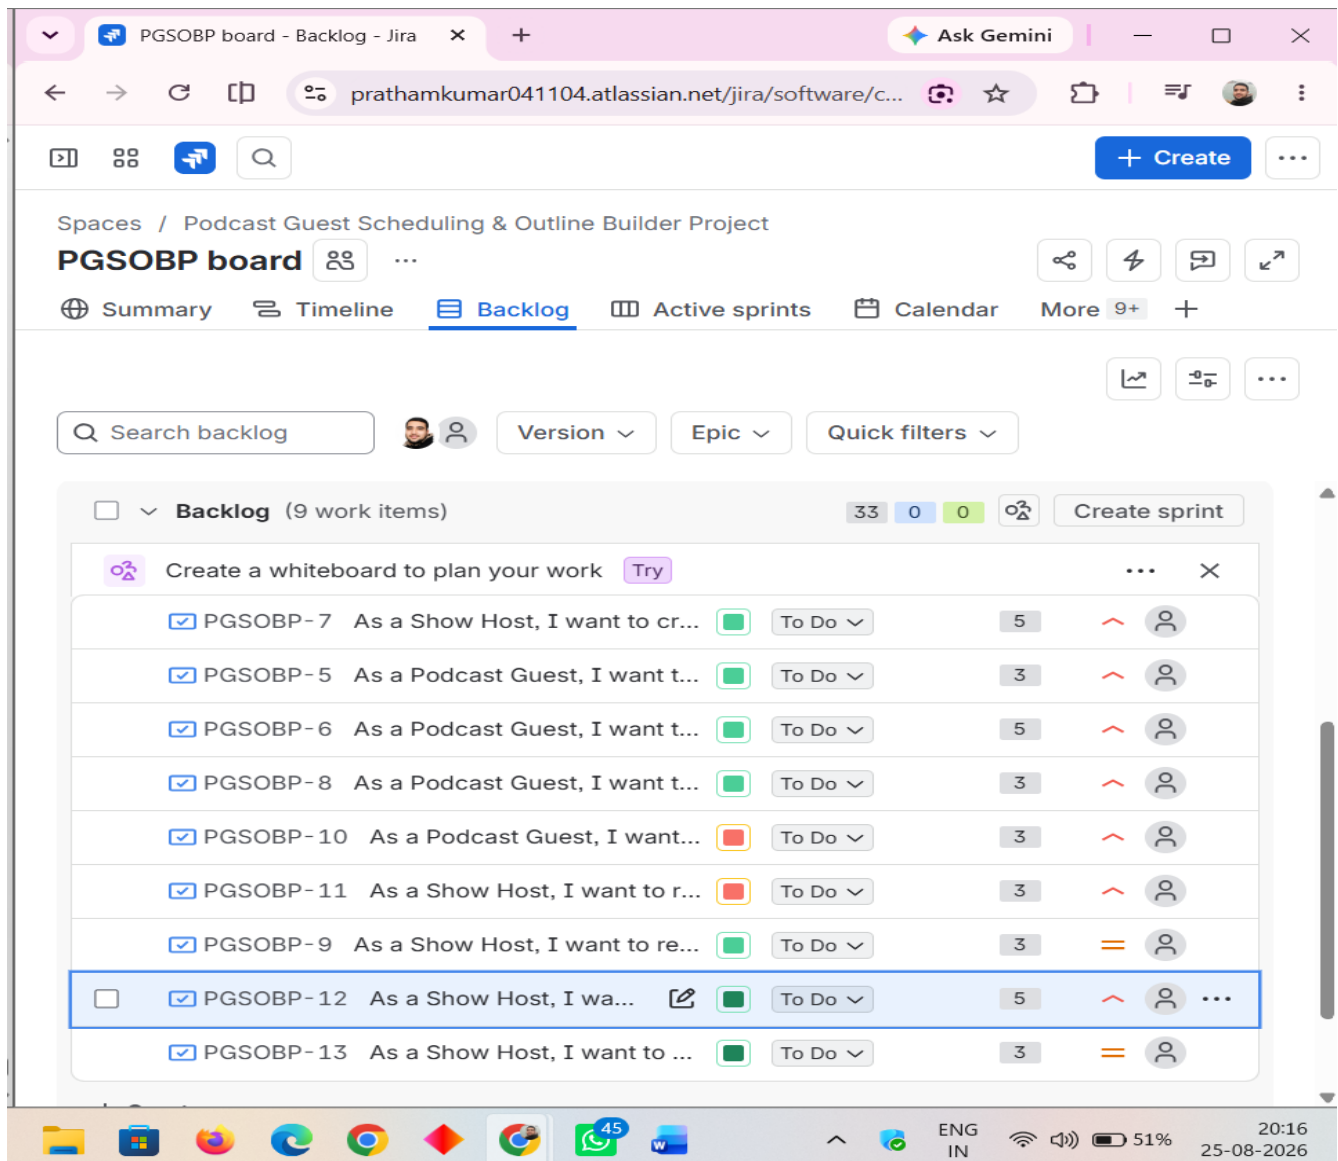

The screenshot shows the Jira interface for the 'PGSOBP board' (Podcast Guest Scheduling & Outline Builder Project). The 'Backlog' tab is selected, displaying 9 work items. The total estimate is 33 story points. The work items are listed in a table with columns for status, priority, story points, and assignee.

Item	Status	Priority	Story Points	Assignee
PGSOBP-7 As a Show Host, I want to cr...	To Do	High	5	[User]
PGSOBP-5 As a Podcast Guest, I want t...	To Do	High	3	[User]
PGSOBP-6 As a Podcast Guest, I want t...	To Do	High	5	[User]
PGSOBP-8 As a Podcast Guest, I want t...	To Do	High	3	[User]
PGSOBP-10 As a Podcast Guest, I want...	To Do	Medium	3	[User]
PGSOBP-11 As a Show Host, I want to r...	To Do	Medium	3	[User]
PGSOBP-9 As a Show Host, I want to re...	To Do	High	3	[User]
PGSOBP-12 As a Show Host, I wa...	To Do	High	5	[User]
PGSOBP-13 As a Show Host, I want to ...	To Do	High	3	[User]



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 1 Planning: Three high-priority and logically related user stories were selected from the product backlog for Sprint 1. These stories cover the creation of interview availability slots, viewing available slots, and booking an interview slot. The selected Sprint 1 backlog contains 3 user stories with a total estimate of 13 story points.

The screenshot displays the Jira interface for the 'PGSOBP board' under the 'Podcast Guest Scheduling & Outline Builder Project'. The 'Backlog' tab is selected, showing a list of user stories. The 'PGSOBP Sprint 1' is active, containing three items with a total estimate of 13 story points. Below the sprint, the 'Backlog' section shows six items, including a whiteboard creation task and several user stories related to guest information and calendar notifications.

Item	Description	Category	Status	Estimate
PGSOBP-7	As a Show Host, I want to create and manage interview availability slots, so that Podcast Guests can book interviews ...	Interview Scheduling	To Do	5
PGSOBP-5	As a Podcast Guest, I want to view available interview slots, so that I can choose a suitable date and time for my podc...	Interview Scheduling	To Do	3
PGSOBP-6	As a Podcast Guest, I want to book an available interview slot, so that I can confirm my podcast interview at a conven...	Interview Scheduling	To Do	5
PGSOBP-8	As a Podcast Guest, I want to submit my biography links and discussion topics, so that the Show Host can prepare rel...	Guest Information	To Do	3
PGSOBP-10	As a Podcast Guest, I want to receive a calendar invitation after booking an interview slot, so that I can keep track of...	Calendar & Notific...	To Do	3
PGSOBP-11	As a Show Host, I want to receive a calendar invitation when a guest books an interview slot, so that I can keep trac...	Calendar & Notific...	To Do	3
PGSOBP-9	As a Show Host, I want to review the guest's submitted biography and discussion topics, so that I can prepare effecti...	Guest Information	To Do	3



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 1 Configuration: Sprint 1 was configured for the period from 25 August to 1 September 2026. The sprint contains three related user stories with a combined estimate of 13 story points. The sprint goal focuses on enabling the Show Host to create interview availability slots and allowing Podcast Guests to view and book suitable interview slots.

The screenshot displays the Jira interface for the 'PGSOBP board' under the 'Podcast Guest Scheduling & Outline Builder Project'. The 'Backlog' tab is selected, showing a list of user stories. The 'PGSOBP Sprint 1' is configured for the period '25 Aug - 1 Sep' with 3 work items. The sprint goal is 'Enable the Show Host to create interview availability slots and allow Podcast Guests to view and book suitable interview slots.' The backlog items are:

- PGSOBP-7: As a Show Host, I want to create and manage interview availability slots, so that Podcast Guests can book interviews ... (Interview Scheduling, To Do, 5 points)
- PGSOBP-5: As a Podcast Guest, I want to view available interview slots, so that I can choose a suitable date and time for my podc... (Interview Scheduling, To Do, 3 points)
- PGSOBP-6: As a Podcast Guest, I want to book an available interview slot, so that I can confirm my podcast interview at a conven... (Interview Scheduling, To Do, 5 points)

The total estimate for the sprint is 13. Below the sprint, the 'Backlog' tab shows 6 work items, including a whiteboard and three more user stories:

- PGSOBP-8: As a Podcast Guest, I want to submit my biography links and discussion topics, so that the Show Host can prepare rel... (Guest Information, To Do, 3 points)
- PGSOBP-10: As a Podcast Guest, I want to receive a calendar invitation after booking an interview slot, so that I can keep track of... (Calendar & Notific..., To Do, 3 points)
- PGSOBP-11: As a Show Host, I want to receive a calendar invitation when a guest books an interview slot, so that I can keep trac... (Calendar & Notific..., To Do, 3 points)

The interface includes a search bar, a 'Create' button, and a 'Quick filters' dropdown. The bottom status bar shows the system time as 20:23 on 25-08-2026, with a battery level of 47% and network status.



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 1 Execution: Sprint 1 was started after completing sprint planning and defining the sprint goal. The active Scrum board displays the selected user stories across the workflow states To Do, In Progress, and Done. Initially, all three Sprint 1 user stories were placed in the To Do state, representing the starting state of sprint execution.

The screenshot displays the Jira interface for the 'PGSOBP board'. The board is set to 'Active sprints' and shows three user stories in the 'TO DO' column. Each story is a card with a description, a label 'Interview Scheduling & Availability Management', a status 'PGSOBP-7', 'PGSOBP-5', and 'PGSOBP-6' respectively, and a priority of 5. The 'IN PROGRESS' and 'DONE' columns are currently empty. The interface includes a search bar, a 'Complete sprint' button, and a 'Group: Story' button. The bottom of the screen shows a Windows taskbar with various application icons and system information like 'ENG IN' and '47%' battery.



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING


5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 1 Report:

The Sprint 1 Report shows the successful completion of the interview scheduling and availability management functionality. All three planned user stories were completed, covering creation of interview availability slots, viewing available slots, and booking an interview slot. The sprint completed a total of **13 story points**, with all planned issues achieving the **Done** status.

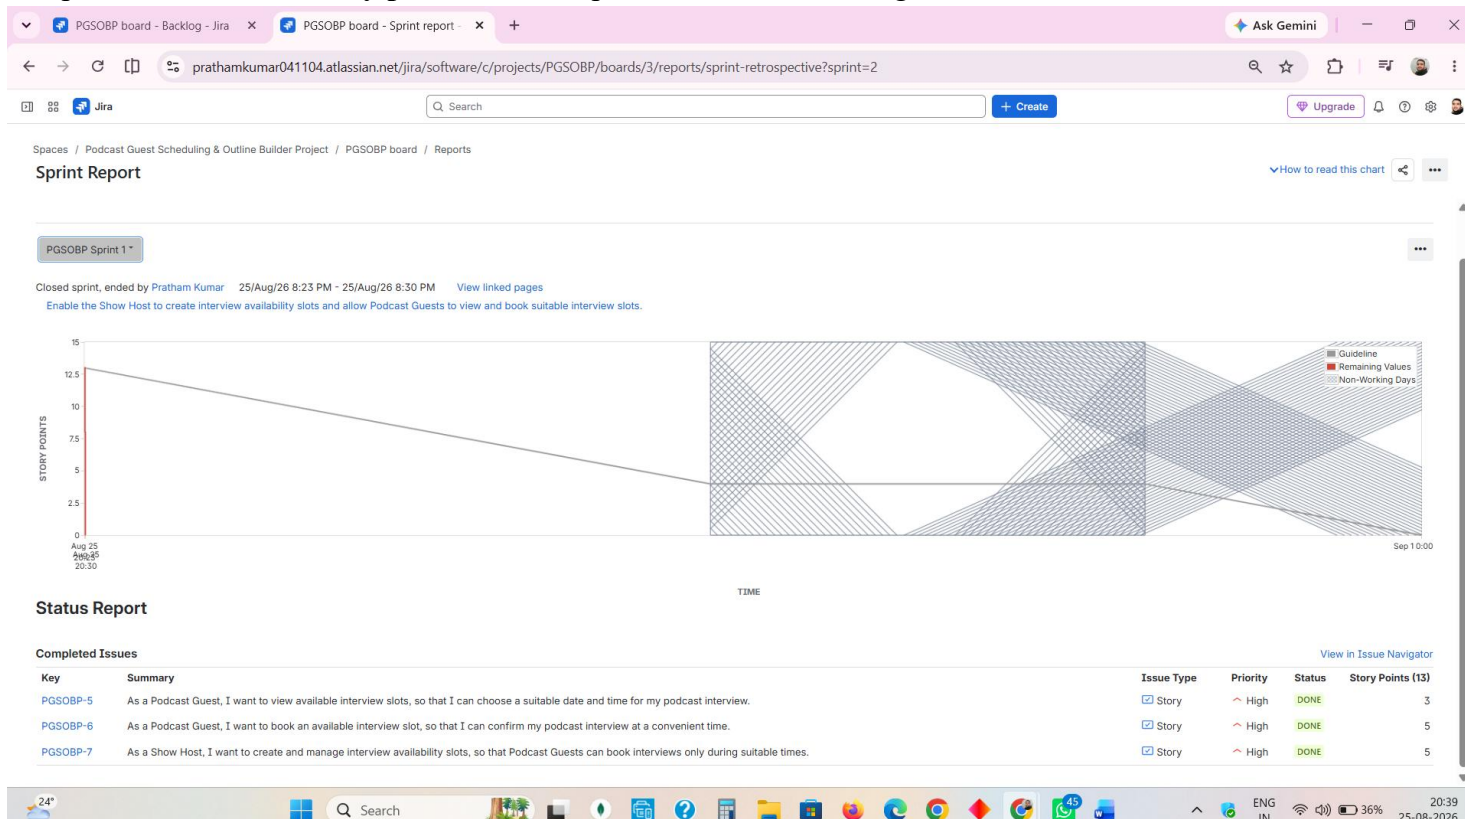



Department of CSE, PES University


UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 2 Report: The Sprint Report shows the completion status of Sprint 2, which focused on guest information collection, calendar notification integration, and episode production preparation. All six planned user stories were completed, accounting for a total of 20 story points. The report provides evidence of the work completed during the sprint and the final status of each user story.

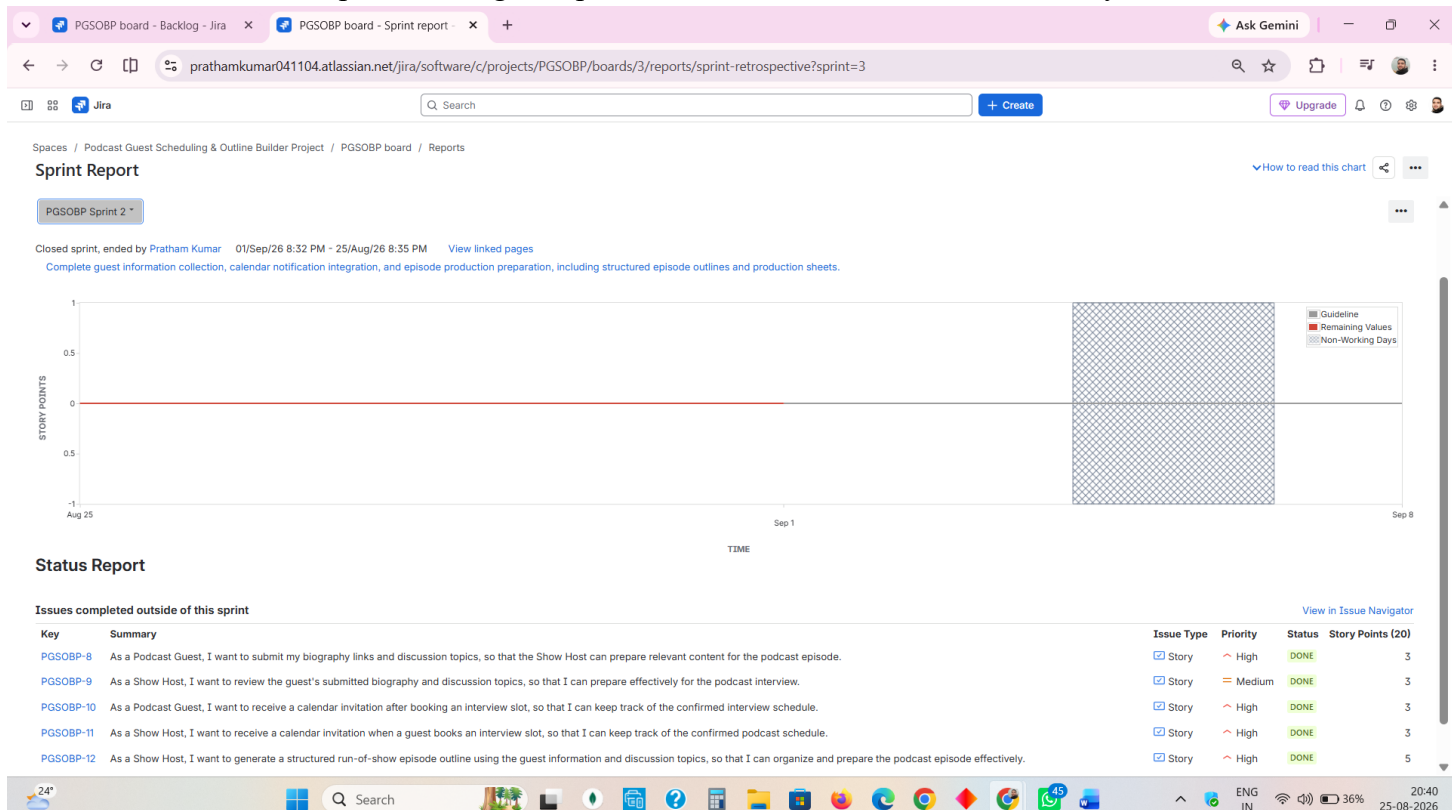



Department of CSE, PES University


UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 1 Burndown Chart: The burndown chart represents the progress of Sprint 1 based on story points. The sprint started with a total of 13 story points distributed across three user stories. As PGSOBP-7, PGSOBP-5, and PGSOBP-6 were completed, the remaining work decreased from 13 to 8, then to 5, and finally to 0 story points. This indicates that all planned work for Sprint 1 was successfully completed.

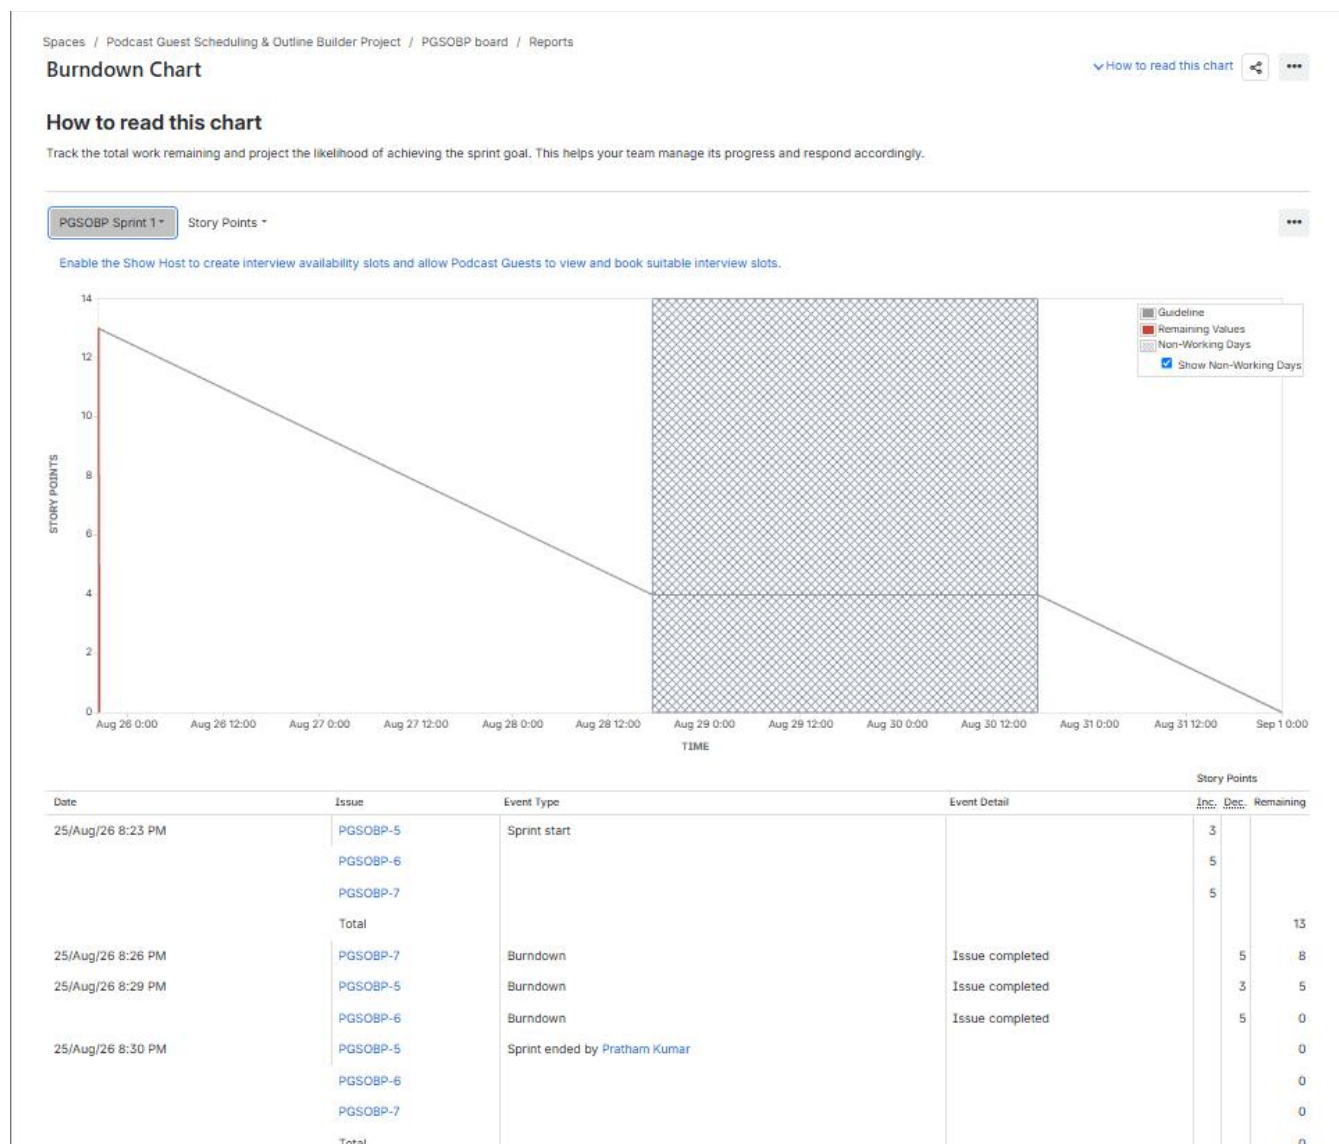



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Sprint 2 Burndown Chart: The burndown chart represents the completion status of Sprint 2, which consisted of six user stories with a total planned effort of 20 story points. All the selected user stories were moved through the sprint workflow and successfully completed. Since the sprint activities were simulated and completed within a short period, Jira records the remaining work as 0 story points, resulting in a flat remaining-value line. The chart therefore confirms the completion of all planned Sprint 2 work.

Spaces / Podcast Guest Scheduling & Outline Builder Project / PGSOBP board / Reports

Burndown Chart


[How to read this chart](#)

How to read this chart

Track the total work remaining and project the likelihood of achieving the sprint goal. This helps your team manage its progress and respond accordingly.

PGSOBP Sprint 2 - Story Points

Complete guest information collection, calendar notification integration, and episode production preparation, including structured episode outlines and production sheets.

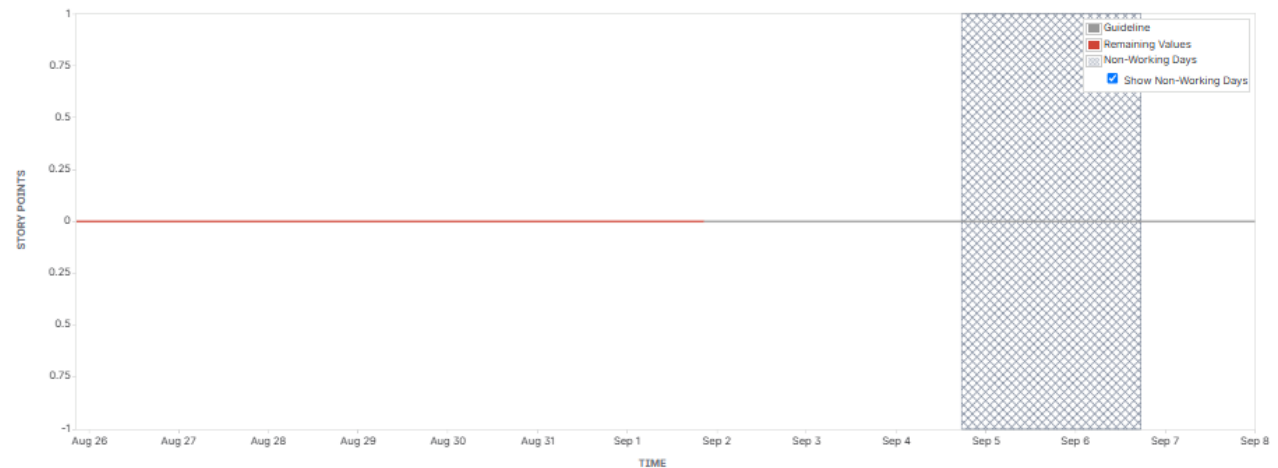

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
01/Sep/26 8:32 PM	PGSOBP-10	Sprint start		0		
	PGSOBP-11			0		
	PGSOBP-12			0		
	PGSOBP-13			0		
	PGSOBP-8			0		
	PGSOBP-9			0		
	Total					0
25/Aug/26 8:35 PM	PGSOBP-10	Sprint ended by Pratham Kumar				0
	PGSOBP-11					0
	PGSOBP-12					0
	PGSOBP-13					0
	PGSOBP-8					0
	PGSOBP-9					0



Department of CSE, PES University

UE24CS341A: SOFTWARE ENGINEERING

5TH SEMESTER, ACADEMIC YEAR 2026-27

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

DATE: 24-08-2026

Reflection Questions: -

1. Did your estimations reflect the actual effort?

Yes, the story point estimations reasonably reflected the expected effort of the user stories. Simpler tasks were assigned **3 story points**, while comparatively complex tasks such as managing interview availability, booking slots, and generating the structured episode outline were assigned **5 story points**. This helped differentiate the effort required for each story and supported sprint planning.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized according to the functional dependencies and importance of the user stories. Core interview scheduling activities were given higher priority and completed in **Sprint 1**, while guest information collection, calendar notifications, and episode production preparation were handled in **Sprint 2**. This ensured that fundamental functionality was addressed before dependent features.

3. How did your simulated sprint align with your plan?

The simulated sprints aligned well with the planned workflow. **Sprint 1 completed 3 user stories totaling 13 story points**, while **Sprint 2 completed the remaining 6 user stories totaling 20 story points**. The stories were progressed through **To Do, In Progress, and Done**, and all planned stories were ultimately completed within their respective simulated sprints.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts showed that the planned workload could be completed within the simulated sprint scope. In **Sprint 1**, the remaining workload decreased from **13 to 8, then 5, and finally 0 story points** as the three stories were completed. Sprint 2 also reached **0 remaining story points** after all six stories were completed. Since the sprint execution was simulated within a short period rather than over several actual working days, the charts do not represent a realistic day-by-day team velocity; however, they clearly demonstrate successful completion of the planned sprint workload.

NAME: PRATHAM KUMAR

SRN NO.: PES2UG24CS368

PRN NO.: PES2202400086

SECTION: F

THANK YOU
